

Bi-weekly Progress Meeting

February 5, 2013

Town of Pittsboro Hillsboro Street Water Main Project • CDBG Project No. 05-D-2087

Date work started: August 15, 2012

Date contract ends: December 13, 2012


Contract amount: \$1,458,125.00

Approximate work completed: SKC, Inc. has installed approximately 6250' of pipe – or about 99% of the total pipe, leaving a little more than 50' to be installed.

Charged to project to date: \$1,071,627.85 (74%)

Discussion Points:

- Street sweeper to clean on Friday mornings
- Traffic control for work in circle this week

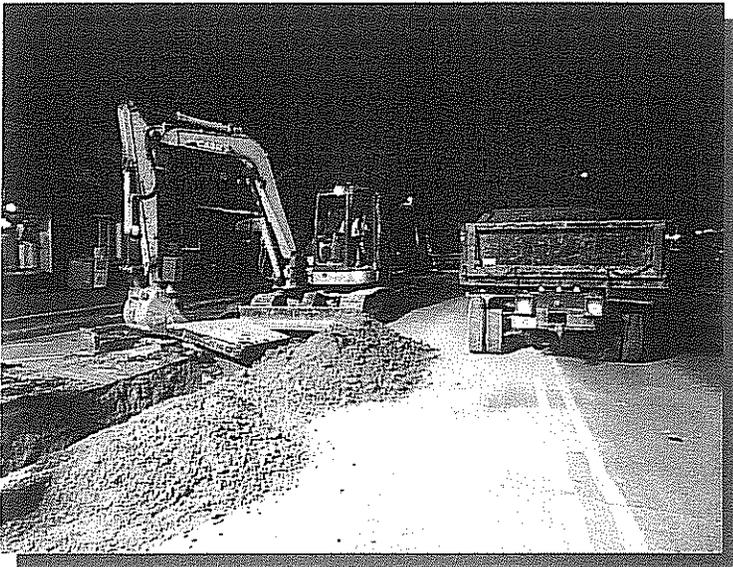

- Temporary parking needed?
- Chlorination & pressure testing this week
- Services: if 2 downtown businesses are on 1 meter, separate?
- Remaining cross lines: Hanks, Lindsey, & Park
- Tie-in's during the day. 2 hour outage, not 6:00 – 8:00 am or 6:00 – 9:00 pm in residential areas and not 6:00am-7:00pm in business area
- Notices distributed
- Investigate sewer line at Midway Street
- Old Courthouse service lines

