


Bi-weekly Progress Meeting

March 5, 2013

Town of Pittsboro Hillsboro Street Water Main Project • CDBG Project No. 05-D-2087

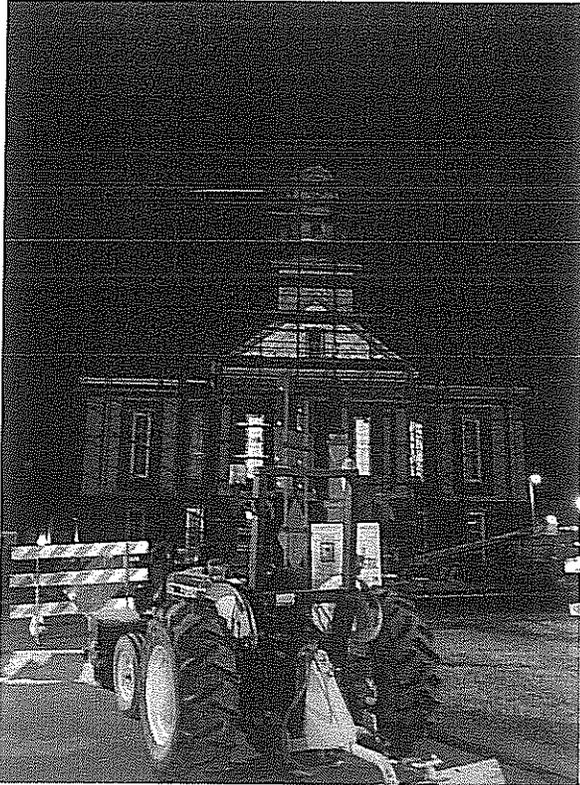

Date work started: August 15, 2012

Date contract ends: December 13, 2012

Contract amount: \$1,458,125.00

Approximate work completed: SKC, Inc. has installed all of the 12" DIP, leaving only a few feet of 6" and 8" that will connect to the main.

Charged to project to date: \$1,300,920.65 (89%)
(Includes Change Order #1)

Work Remaining:

- Abandon 2" in circle
- Hydrant leg at Sanford Road & Virlie's
- Pour thrust blocks in circle
- Tie-in 2" on Launis
- Investigate sewer line at Midway Street & install manhole
- Install sewer for Mill
- Abandon/grout 10" AC line, remove valve boxes
- Clean-up at Tank Site
- Meter at Old Courthouse this week, 6" valves at ROW
- Investigate 8" mis-connection at Mill vault
- Grading & seeding
- Flowable fill
- Asphalt

- Pressure test line from Virlie's to circle
- Chlorinate line from Virlie's to circle
- Install 35 services – from Lindsey to Courthouse (all services north of Lindsey are complete)
- Tie-in cross connections at Park, Hanks, Thompson, East & West Salisbury
- Tie-in at circle for Sanford Road & West St.

