


**Bi-weekly Progress Meeting
May 14, 2013**

Town of Pittsboro Hillsboro Street Water Main Project • CDBG Project No. 05-D-2087

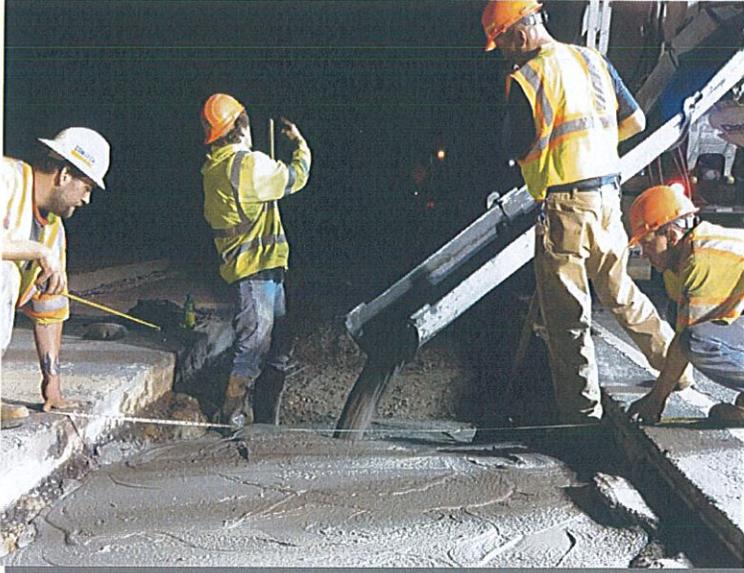

- Total project construction cost through May 1, 2013 is \$1,539,636.45 (105%).
- Contract \$1,458,125.00

Work Remaining:

- Abandon/grout 10" AC line
- Clean-up at Tank Site
- Grading & seeding
- Road repair

Inside 6" water main on Sanford Road.

